Activity Name	Remaining Duration	Start	Finish	CM21 RESP. PARTY
CONTRACT E2 (SPN 92-619)	61	22-Oct-08 A	29-Nov-11	
CONTRACT E2 - OVERVIEW	61	22-Oct-08 A	29-Nov-11	
Contract E2 - Construction	61	22-Oct-08 A	29-Nov-11	
Contract E2 - Contract Completion Date	0		29-Nov-11*	CM-E2-02
Contract E2 - Notice-to-Proceed	0	22-Oct-08 A		CM-E2-01
CONTRACT STAGES & TRAFFIC SHIFTS	2	25-Feb-09 A	05-Oct-11	
Shift I-95NB Traffic West to Begin Pier P-4	0	25-Feb-09 A	26-Feb-09 A	
Shift Ramp H Traffic to Final Align. on Br. 952	2	04-Oct-11	05-Oct-11	
Shift Rt. 34WB (Ramp L) Traffic North on Br. 952	0	10-Jun-10 A	11-Jun-10 A	
Shift Rt. 34WB (Ramp M) Traffic North on Br. 952	0	11-May-10 A	12-May-10 A	
Shift Rte. 34WB Traffic to South Side of Br. 952	0	29-May-09 A	31-May-09 A	
MILESTONES	0	24-Mar-09 A	07-Jun-11 A	
Close Existing I-95SB On-Ramp from Brewery St.	0		24-Mar-09 A	TM-09
Close Existing Rte. 34EB Off-Ramp to Brewery St.	0		24-Mar-09 A	TM-10
Open Exist. I-91SB to I-95SB to 2 Lanes Traffic	0		17-Apr-10 A	PM-12(I)
Open New I-95 to Rte. 34 WB (Ramp H) to Traffic	0		07-Jun-11 A	TM-12
CONSTRUCTION ACTIVITIES	50	14-Jan-09 A	18-Nov-11	
Bridge No. 00166 Stage 1 SB Widening	0	14-Jan-09 A	10-Sep-09 A	
Bridge No. 00166 Stage 2A Median Reconfiguration	0	13-Oct-09 A	12-Nov-09 A	
Bridge No. 00166 Stage 3 NB Widening	0	16-Nov-09 A	25-Jul-10 A	
Bridge No. 00166 Stage 4 Deck Reconstruction	0	02-Aug-10 A	21-Feb-11 A	
Bridge No. 00952 Stage 1 Construction	0	10-Jun-09 A	10-May-10 A	
Bridge No. 00952 Stage 2A Construction	0	29-Jun-10 A	03-Dec-10 A	
Bridge No. 00952 Stage 5B Construction	4	06-Dec-10 A	03-Oct-11	
Construct Bridge No. 00169 Abutment 1	0	02-Jun-09 A	21-Dec-09 A	
Construct Bridge No. 00169 Abutment 2	0	14-Sep-09 A	19-Apr-10 A	
Construct Bridge No. 00169 Pier P-1	0	07-Jul-09 A	02-Mar-10 A	
Construct Bridge No. 00169 Pier P-2	0	23-Apr-09 A	01-Oct-09 A	
Construct Bridge No. 00169 Pier P-3	0	01-Apr-09 A	23-Sep-09 A	
Construct Bridge No. 00169 Pier P-4	0	08-Apr-09 A	10-Sep-09 A	
Construct Bridge No. 00169 Pier P-5	0	13-Oct-09 A	26-Jan-10 A	
Construct Bridge No. 00169 Pier P-6	0	16-Oct-09 A	18-Feb-10 A	
Construct Bridge No. 00169 Pier P-7	0	09-Nov-09 A	09-Mar-10 A	
Construct Bridge No. 00169 Superstructure	0	08-Mar-10 A	06-Jun-11 A	
Construct Bridge No. 00172 Abutment 1	0	30-Oct-09 A	15-Jul-11 A	
Construct I-95NB Off-Ramp to L.Wharf Dr.(Ramp A)	0	04-Jan-10 A	24-Jun-10 A	
Construct I-95SB Off-Ramp to Sargent Dr.(Ramp D)	0	14-Sep-09 A	22-Jan-10 A	TM-11
Construct L.Wharf Dr. On-Ramp to I-95NB(Ramp C)	0	08-Mar-10 A	10-Sep-10 A	
Construct Retaining Wall 109	0	25-May-10 A	03-Aug-10 A	
Construct Retaining Wall 128	0	04-Jan-10 A	29-Aug-10 A	
Construct Retaining Wall 129	0	15-May-09 A	04-Jan-10 A	
Construct Retaining Wall 130	0	27-Apr-10 A	15-Jul-10 A	
Construct Retaining Wall 131	0	11-Aug-09 A	10-Sep-09 A	
Construct Retaining Walls 119 & 120	0	10-Aug-09 A	18-Jul-10 A	
Construct Sargent Dr. On-Ramp to I-95 SB(Ramp B)	0	01-Jul-09 A	20-Sep-09 A	
Water Street Sewer & Drainage Construction	50	04-Apr-11 A	18-Nov-11	

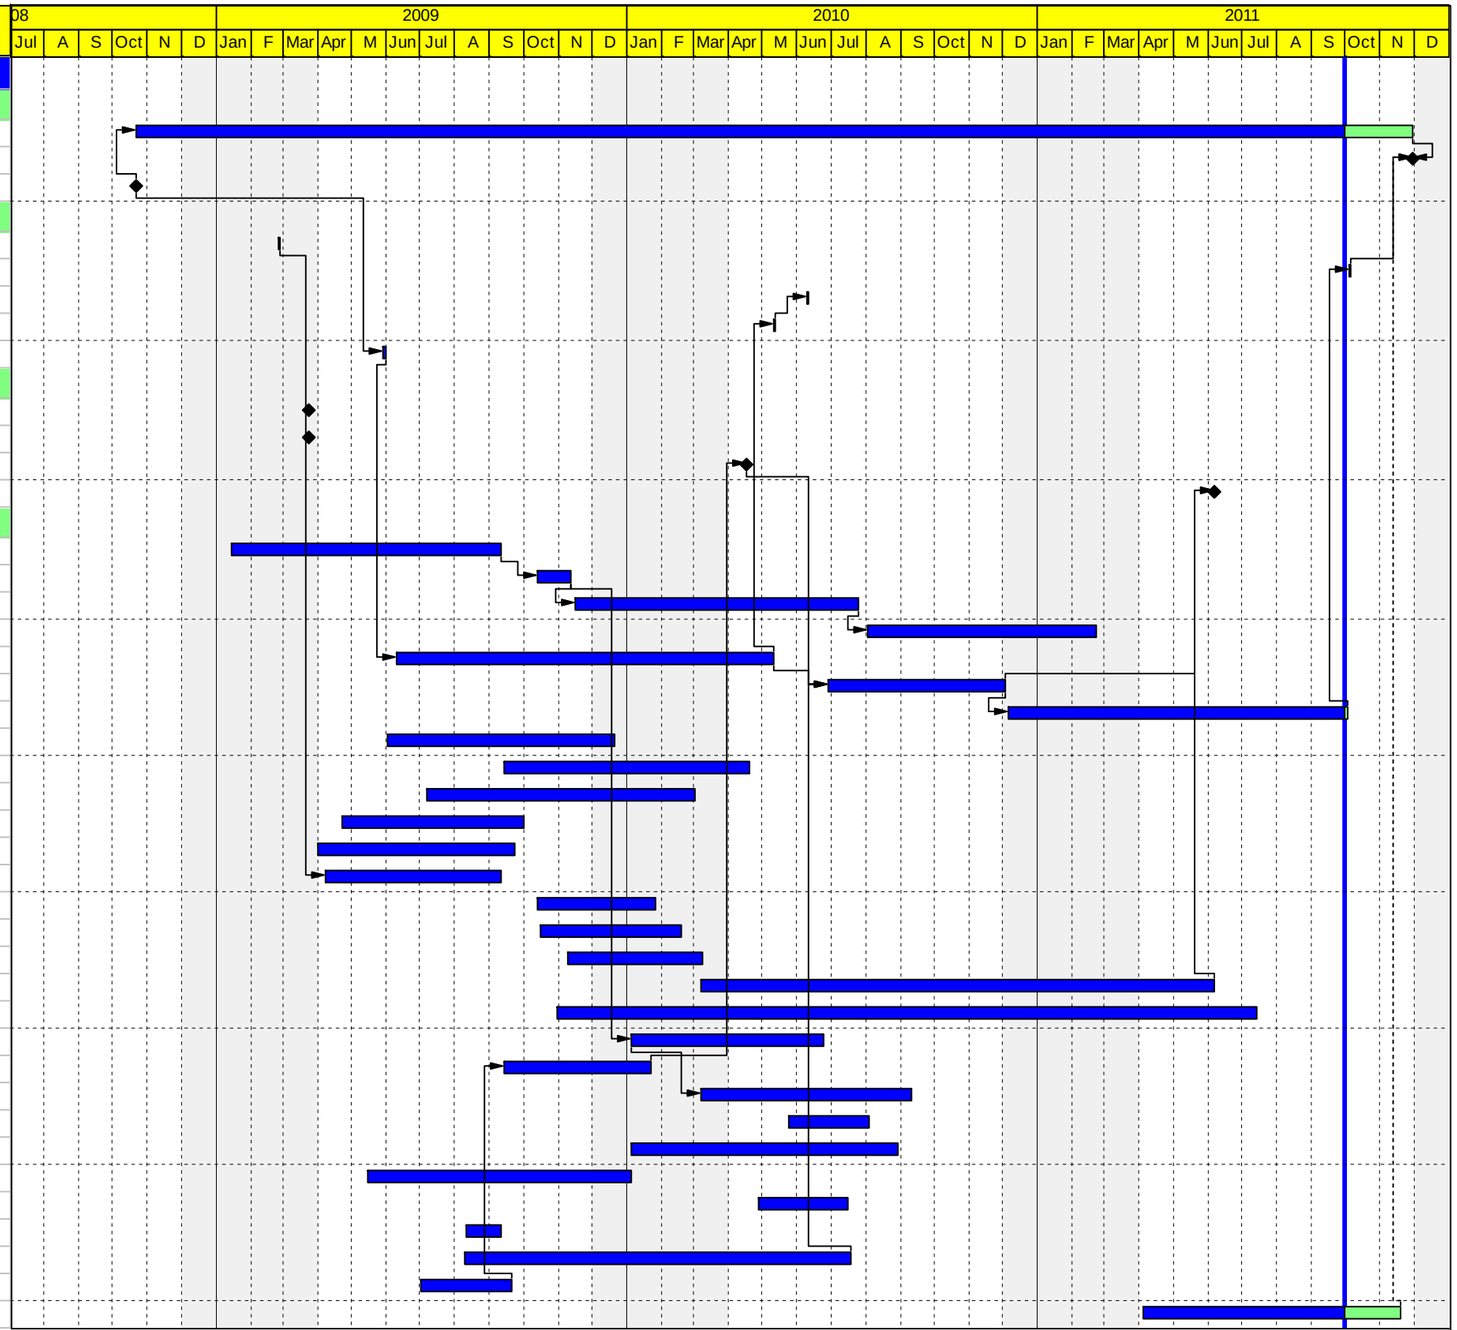

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

I-95 NEW HAVEN HARBOR CROSSING

CORRIDOR IMPROVEMENT PROGRAM

CONTRACT E2 SUMMARY SCHEDULE E

Date	Revision	Checked	Approved
01-Oct-11	October 2011 Website Update	DFA	
